

Hilland Environmental

Environmental Assessment Practitioners

166 Mount View, Victoria Heights
P.O. Box 590, GEORGE, 6530
Western Cape, South Africa

Tel: +27(0)44 889 0229
Fax: +27 (0) 86 542 5248
Mobile: + 27 (0) 82 5586 589
E-mail: info@hilland.co.za
www.hilland.co.za

ENVIRONMENTAL COMPLIANCE MONITORING REPORT NO.10

FOR

OUTENIKUASBOSCH, FARMS OUTENIKUASBOSCH 149 AND HARTENBOSCH
217, HARTENBOS

CIVIL SERVICES INSTALLATION (PHASE 10)



OUTENIKUASBOSCH
The Wildlife Village

Compiled by:

Hilland Environmental

Reference:

MOS21/455/23

Report Period:

October 2021

ISSUED BY:

HillLand Environmental

PO Box 590

George, 6530

Tel: 044 889 0229

Fax: 086 542 5248

E-mail: cathy@hilland.co.za / admin@hilland.co.za / environmental@hilland.co.za

Website: www.hilland.co.za

OUTENIKUASBOSCH, FARMS OUTENIKUASBOSCH 149 AND HARTENBOSCH 217, HARTENBOS

**ENVIRONMENTAL MONITORING REPORT NO 10
OCTOBER 2021**

Conditions of report use:

The report is the property of the sponsor and the author, who may publish it, in whole, provided:

- 1 That written approval is obtained from the author and that **HillLand Environmental** is acknowledged in the publication;
- 2 That **HillLand Environmental** is indemnified against any claim for damages that may result from publication;
- 3 The contents of this report may not be used for purposes of sale or publicity or advertisement without the prior written approval of **HillLand Environmental**.
- 4 That it is understood that **HillLand Environmental** accepts no responsibility for the contractor's failure to follow the recommended programme.
- 5 That it is understood that **HillLand Environmental** accepts no responsibility for the contractor's deviation or non-compliance to any specifications or guidelines provided in the report.
- 6 That it is understood that all figures, plates, and diagrams are copyrighted and may not be reproduced by any means, in any form, in part or whole.

Submitted to:	Luxolo Kula – DEADP (Cape Town) Dryer van Zyl – Owner / Developer ZEC4 (Pty) Ltd
Copies to:	Deon Brand – Outeniquasbosch Petrie van Zyl – Move It Civils (Contractor – phase 10) Charl Moller – Charl Moller Consulting Engineer

Environmental Monitoring Report No. 10

This report monitors compliance against the Environmental Management Plan (Ref.: MOS18/455/01). This monitoring report constitutes the 10th Environmental Monitoring Report and covers inspections done during October 2021 for the **civil services installation of Phase 10**.

This ECO report covers compliance monitoring for all works to date in terms of the EMPr and the EA in relation to civil services installation.

Commencement of **all listed activities** for the development (including the Resort zone) has taken place in accordance with the EA. The main road to the resort area has been constructed and the decking at the first resort unit complies with the aesthetic requirements.

Weekly ECO monitoring takes place during civil services construction phase (**phase 10**) and monthly during individual **house** construction.

The **Operational phase has started** with some residence residing permanently within Outeniquasbosch. It is now important to ensure that all construction areas are demarcated appropriately to prevent any unauthorised entry or accidental injury (residents and animals). All effort should be made to ensure that the estate is always kept neat and tidy, this includes litter, construction rubble and management of invasive alien plants and weeds.

1. Environmental Induction

Environmental induction was done with all staff members on-site in **March 2021** and **14 October 2021** with the curb sub-contractor (LNJ Civils). The contractor must notify the ECO when new staff is to start on site to arrange an environmental induction session.

2. NO-GO Demarcation

No-Go areas were discussed during the environmental induction.

Demarcating open trenches have been disused and the owner requires the following:

- *Game generally stays away from excavations and therefore the main focus regarding demarcation of excavations relate to person safety. Ongoing monitoring of the game movement and activity is the responsibility of the owner and demarcation must be installed upon instruction from the said owner.*

3. Fauna and Flora

The civil and building contractors have to ensure that no harm or damage is done to any fauna or flora during active construction periods. Harm or damage can be mitigated by conducting a survey of the area to be excavated or cleared to ensure that no animals or plants are affected.

A plant search and rescue are to be arranged with the ECO if there are any plants within the specific site that require rescue – no plant search and rescue was required during this reporting period.

Ongoing eradication of listed invasive alien plants must be considered high priority to prevent the spread of any of these species.

- *Alien invasive plant species as a result of construction (all phases) activity must be removed - the ECO will inform if and when alien plants are noted. The developer/management team must ensure ongoing alien plant eradication.*

4. Soil & Site Management

The contractors should note that the topsoil must be kept separate from any other subsoil or construction material to prevent contamination.

- *No issues noted during the reporting period.*
- *Topsoil is replaced and re-vegetation/seeding is now required (refer to rehabilitation section)*
- *Dust mitigation measures (keeping the roads wet) are implemented when dust becomes an issue.*



2021.10.28 – Ongoing construction of the roads in phase 10.



2021.10.14 – Ongoing construction of the roads in phase 10.



2021.10.22 – The installation of the curbs in phase 10.



5. Heritage Requirements

Should any heritage remains be exposed during excavations or any actions on the site, these must immediately be reported to the Provincial Heritage Resources Authority of the Western Cape, Heritage Western Cape (in accordance with the applicable legislation). Heritage remains uncovered or disturbed during earthworks must not be further disturbed until the necessary approval has been obtained from Heritage Western Cape. Heritage remains include: archaeological remains (including fossil bones and fossil shells); coins; indigenous and/or colonial ceramics; any articles of value or antiquity; marine shell heaps; stone artifacts and bone remains; structures and other built features; rock art and rock engravings; shipwrecks; and graves or unmarked human burials.

A qualified archaeologist must be contracted where necessary (at the expense of the applicant and in consultation with the relevant authority) to remove any human remains in accordance with the requirements of the relevant authority.

- No heritage remains have been discovered to date.

6. Construction Site Camp

Contractors (civil and house construction) must provide ablution facilities for all construction personnel working on the site. One facility for every 15 persons on site is required.

- Toilet facilities are available on site during civil services installation.



2021.09.23 – Phase 10 contractor provides a portable chemical toilet for all staff.



2021.10.28 - The bin must be emptied before the plastic is blown away by the wind.

A fenced off area must be created within the camp site for refuse and waste management as indicated above. ECO to inspect for compliance.

- Adequate litter bins are to be provided at the site camp; littering should be covered in regular "toolbox" talks with all staff members.
- Please ensure that the plastic rapping of cement bags, brick, curbs etc are stored of in a bin/skip that is covered.

No accommodation of contractors or their staff except for a night watchman is permitted on site.

- No accommodation on site.

Any concrete batching areas are to be approved by the ECO prior to utilization and must be equipped with suitable settling ponds and trapping mechanisms to ensure that contaminated water does not leave the restricted area.

- Concrete mixing for the curbs area done in the road surface. No issues with regards to runoff water was noted.

Any temporary diesel storage tanks are to be secured with adequate bunding to cater for spillage and leakage

- No fuel is being stored on site to the knowledge of the ECO.

There should be a secure access point to the construction site in order to ensure that no unauthorized entry is permitted which may lead to a safety or security risk.

- Access to Outeniquasbosch Eco Estate is controlled through access-controlled gates/booms.

Any temporary haul roads or access roads for construction need to be maintained at all times by the contractor.

- The contractor is maintaining the current construction haul road. Please be reminded that driving off the designated haul roads or access roads **is not permitted**.
- Construction vehicles must **abide to the speed limit** as this is a wildlife estate with animals roaming freely.

7. Rehabilitation at stormwater outlet structures


The following rehabilitation recommendation relates to the completed stormwater outlet structures within phase 10 which was discussed at the site meeting – the estate management are busy with rehabilitation:

- Create small soil or stone berms across to slow the flow of the surface water;

- Sow the indigenous grass seed mixture on the side slopes and above the structure areas;
- Mulch filled onion bag (or similar) pegged along the contours, to the side slopes (where steep)
- Estate Management - ongoing maintenance of the stormwater outlets are to be done.

Indigenous grass seed mixture:

Equal parts of: **2g/m²** Kweek grass (*Cynodon dactylon*) seed and **2g/m²** Oulandsgras/Weeping Love Grass (*Eragrostis curvula*) seed (approximately **4g/m²**) that is to be sown over loosely raked soil.

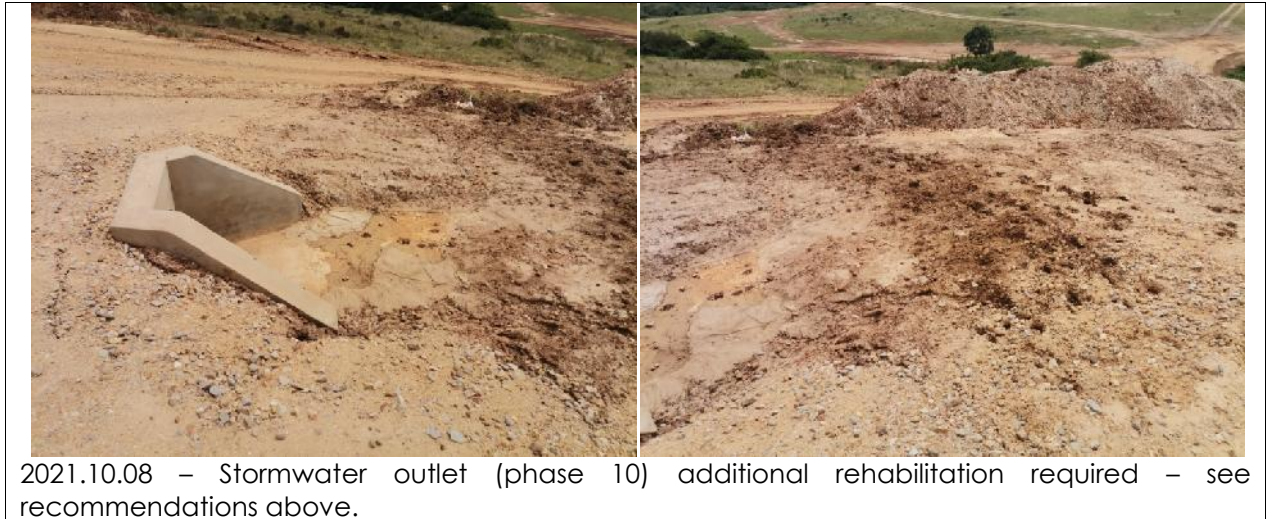

8. Conclusion

No environmental damage or issues noted during ECO site inspections.

The contractor is aware of the environmental requirements and are complying. It is advised that the contractors do regular toolbox talks with all staff members with special focus on **littering and cigarette** butt disposal. The **building** contractors are also reminded to ensure that the No-Go demarcation and safety netting is maintained to ensure that no animals get injured.

ECO monitoring for during **October** 2021

Date:	Comment:
8 October 2021	ECO site inspection of the Civil contractor
14 October 2021	ECO site inspection of the Civil contractor
22 October 2021	ECO site inspection of the Civil contractor
28 October 2021	ECO site inspection of the Civil contractor & Houses
